South Coast Septic to Sewer
Rincon Point
Design Schedule
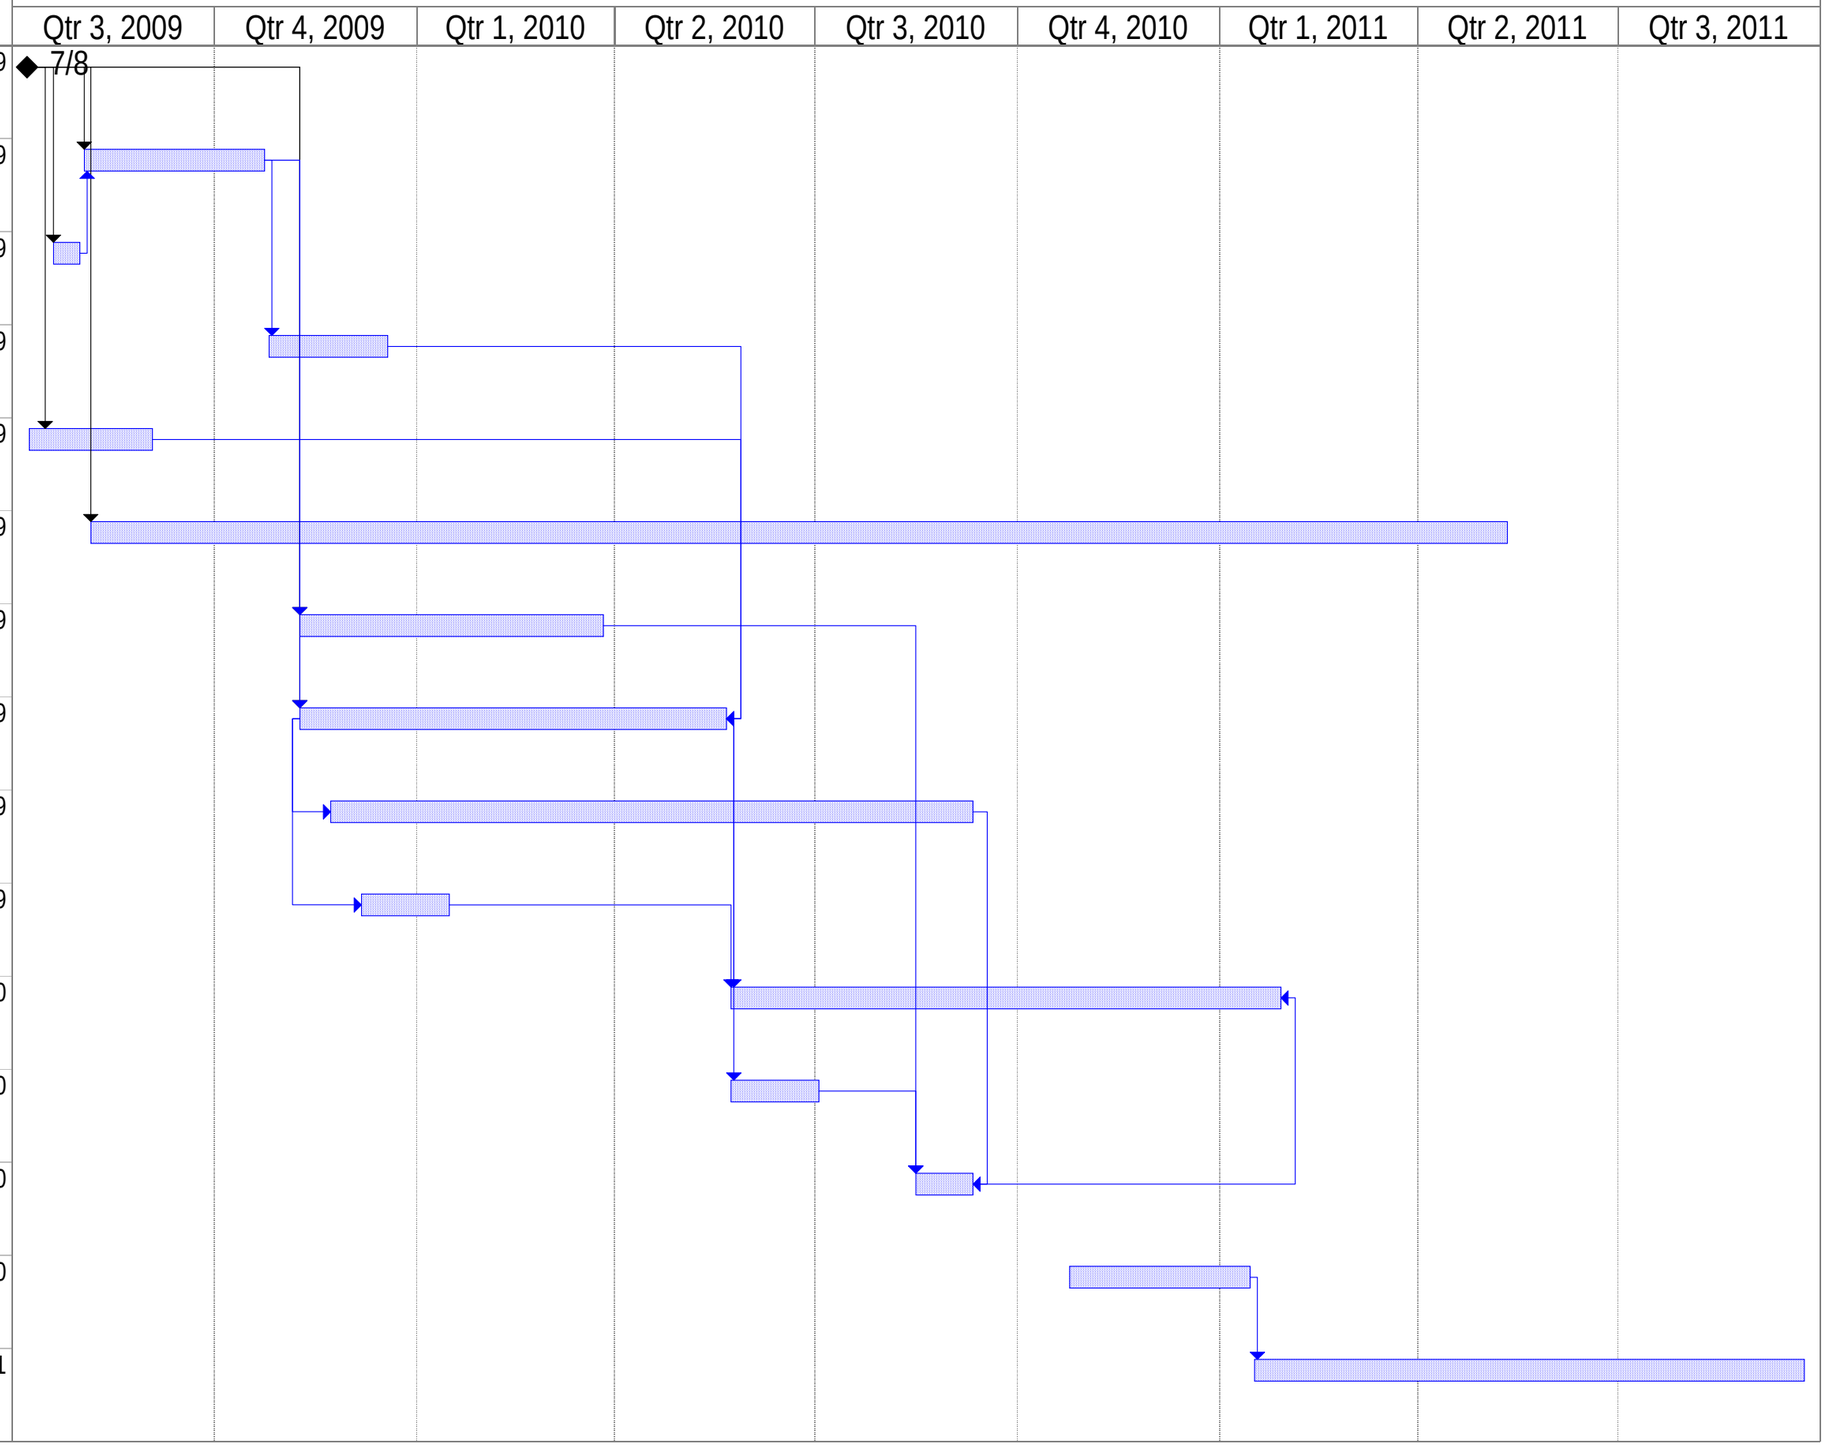
ID	Task Name	Duration	Start
1	Notice to Proceed	1 day	Wed 7/8/09
2	Topographic Mapping	60 days	Mon 8/3/09
3	Geotechnical Field Work	10 days	Mon 7/20/09
4	Geotechnical Reports	40 days	Mon 10/26/09
5	Design Criteria & Pump Rec'dn	40 days	Thu 7/9/09
6	Public Information/Community Liaison	460 days	Thu 8/6/09
7	Rincon Pump Sta & Gen Bldg Design	100 days	Mon 11/9/09
8	50% Plans, Specs & Estimates	140 days	Mon 11/9/09
9	Local Agency Permitting/Approval	210 days	Mon 11/23/09
10	Caltrans Initial Discussions	30 days	Mon 12/7/09
11	Caltrans Encroachment Permit	180 days	Mon 5/24/10
12	90% Plans, Specs & Estimates (PS&E)	30 days	Mon 5/24/10
13	100% PS&E - Bid Documents	20 days	Mon 8/16/10
14	Bidding & Award of Construction Contract	60 days	Mon 10/25/10
15	Construction	180 days	Mon 1/17/11
